


# Rutherford Street Stormwater Upgrade



## Update Six – February 2023

### Smooth progress made on Rutherford Street upgrade

The new year kicked off with another milestone for the project, completing the asphalt re-surfacing for the main carriageway along Waimea Road and Rutherford Street. In the coming weeks, you may notice the site is a lot smaller compared to the size of the site last year. The project is making great progress, but there are still a few tasks left before the project is finished.

### Traffic island reinstatement


One task is reinstating the pedestrian refuge immediately in front of Nelson College for Girls, as well as the other traffic islands along Rutherford Street. The new refuge will be an improvement on the old version as it will be built to modern safety standards.

The watermain and sewer works are currently being

completed outside Rutherford Street Kindergarten. Once these are complete, the traffic island at the bottom of Bronte Street will also be constructed. Asphalt resurfacing works are scheduled along Waimea Road footpath for the week starting 13 February.

### Van Diemen Street intersection

At the intersection of Van Diemen Street and Rutherford Street, we are completing some minor works, including widening the road to improve safety and upgrading the stormwater network. The traffic islands, linemarking and signs at this intersection will also be put back in place before the road is fully reopened. To complete the asphalt resurfacing at this intersection, we will once again need to close one lane out of Ngatitama Street, similar to what the detour was earlier in the project. The road will only need to be closed for up to two weeks, starting Tuesday 7 February. Please see the map below for details.

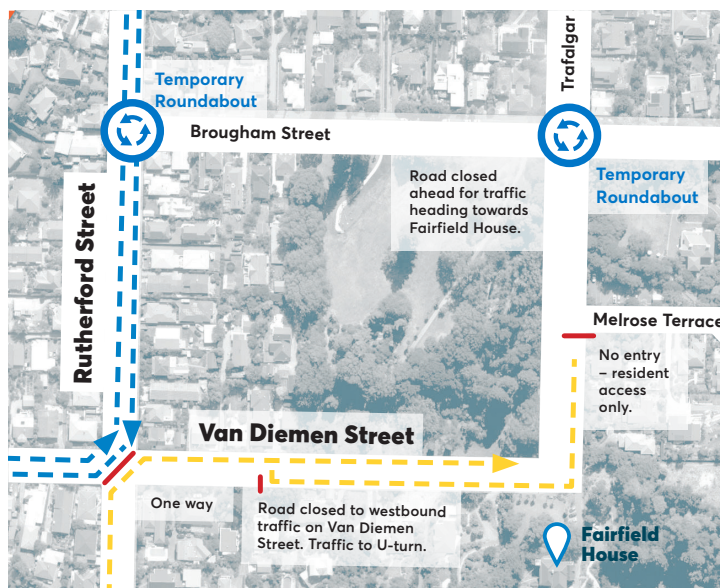

### Finishing up

Once the construction activities are complete, temporary roundabouts, including signs and road markings, will be removed.

Work is on track, and we are scheduled to finish up before the end of February – weather dependent – well ahead of the original programme!

We would like to thank all residents, businesses and the general public for their cooperation during the project.

### Contacts

**Construction queries or reporting urgent issues:**  
Fulton Hogan on 027 456 7654

**General queries:** Nelson City Council on 03 546 0200  
**Email:** [projects@ncc.govt.nz](mailto:projects@ncc.govt.nz)
